

**KEY**


-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase I - Ground Floor      June 21, 2010 – August 27, 2010**





- Start Foundations for North Stair Tower Addition
- Start Foundations for New Bridge Addition

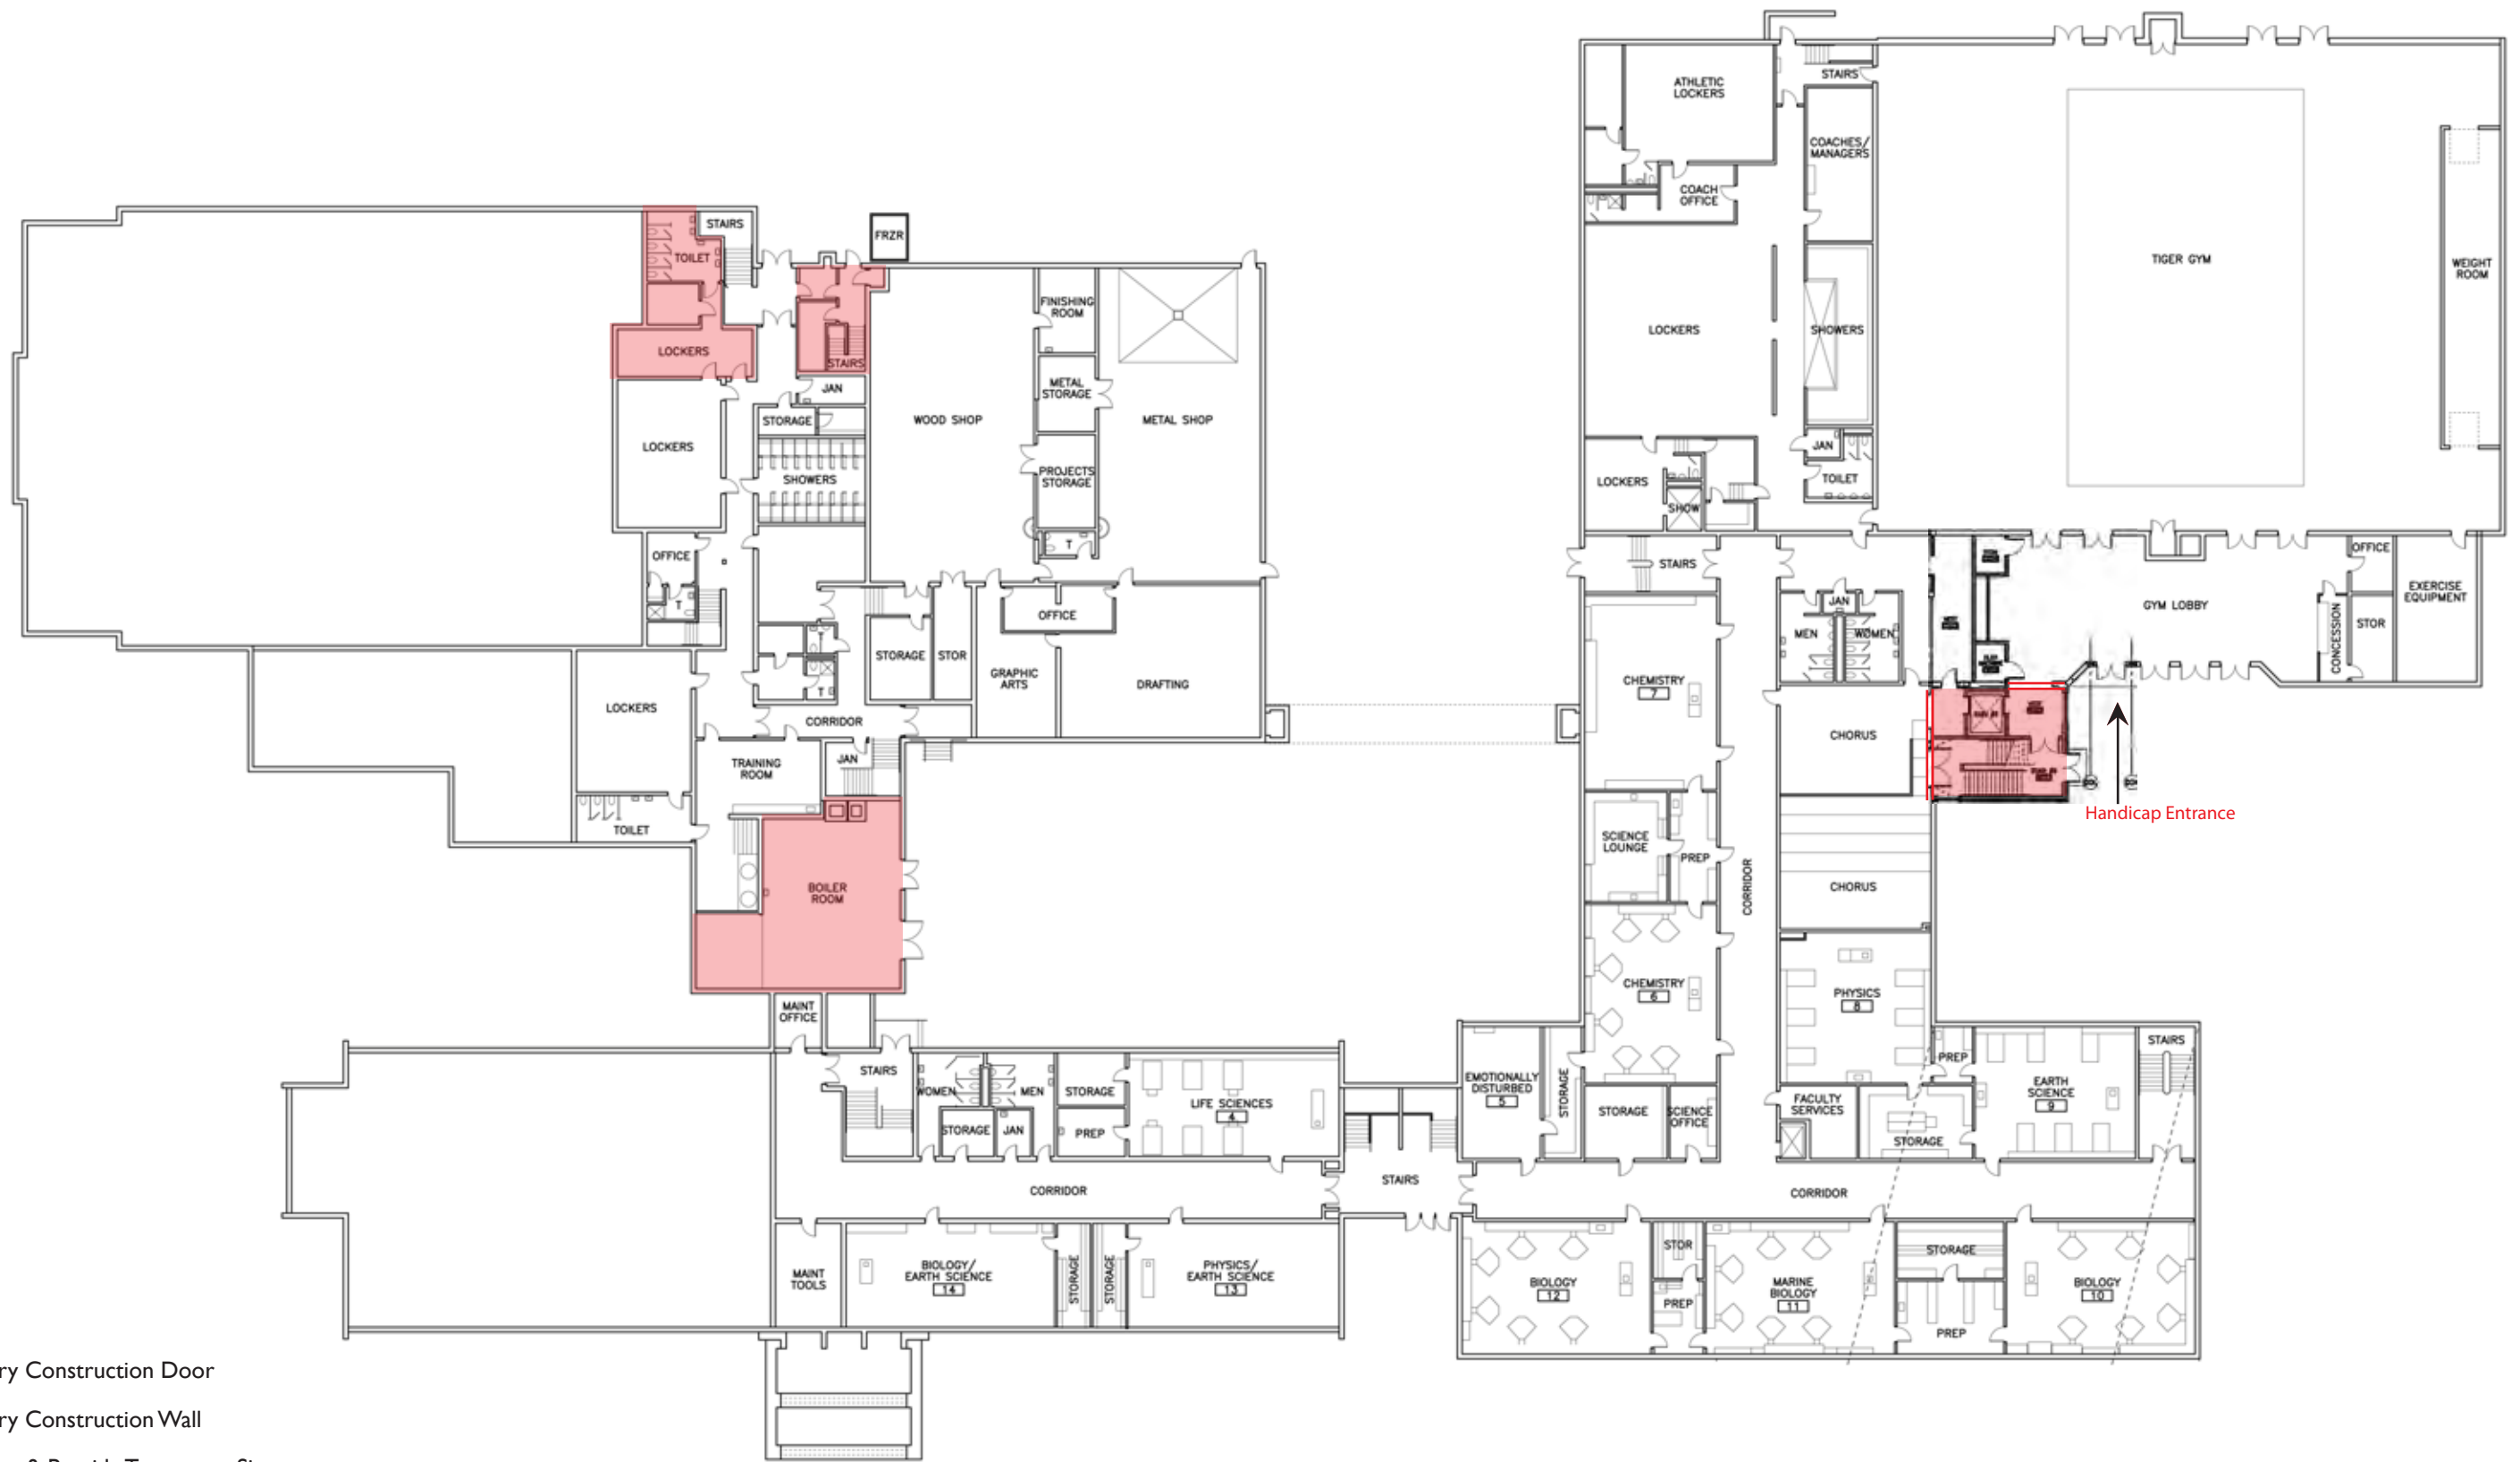

June 9, 2010



**KEY**

-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 2 - Ground Floor      August 30, 2010 – December 23, 2010**

- Continue Work on North Stair Tower Addition
- Renovate Old Storage & Stair to New Electric Room
- Start Work in Boiler Room



June 9, 2010



**KEY**

-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 3 - Ground Floor      January 3, 2011 - April 15, 2011**



- Continue Working on New Electric Room & Boiler
- North Stair Tower Open for Use (Excluding Elevator)



June 9, 2010



**KEY**

-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 4 - Ground Floor April 25, 2011 – June 17, 2011**





- Continue Working on New Electrical & Boiler Rooms
- Start renovation of Second Block of Classrooms Leaving Egress Stair Operational



June 9, 2010



**KEY**

-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 5 - Ground Floor June 20, 2011 – August 26, 2011**

- Renovate Adult Ed. in Basement (Not Shown)
- Renovate Biology and Earth Science Classrooms
- School Reoccupies Second Classroom Block and Science Classrooms before School Starts in the Fall



June 9, 2010



- KEY**
-  Temporary Construction Door
  -  Temporary Construction Wall
  - L & S** Lock Door & Provide Temporary Signage
  -  Construction Area
  -  Completed Construction

**Phase 6 - Ground Floor September 6, 2011 – November 18, 2011**

- School Re-occupies Second Block & Chemistry Rooms Before School Starts in the Fall
- Renovations of Old Women's Locker Rooms to Custodial Storage & Utility Space



June 9, 2010



**KEY**


-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 7 - Ground Floor November 28, 2011 – April 20, 2012**



- Renovate Fourth Classroom Block, Earth Science and Physics Labs
- School Reoccupies Fourth Classroom Block at Spring Break

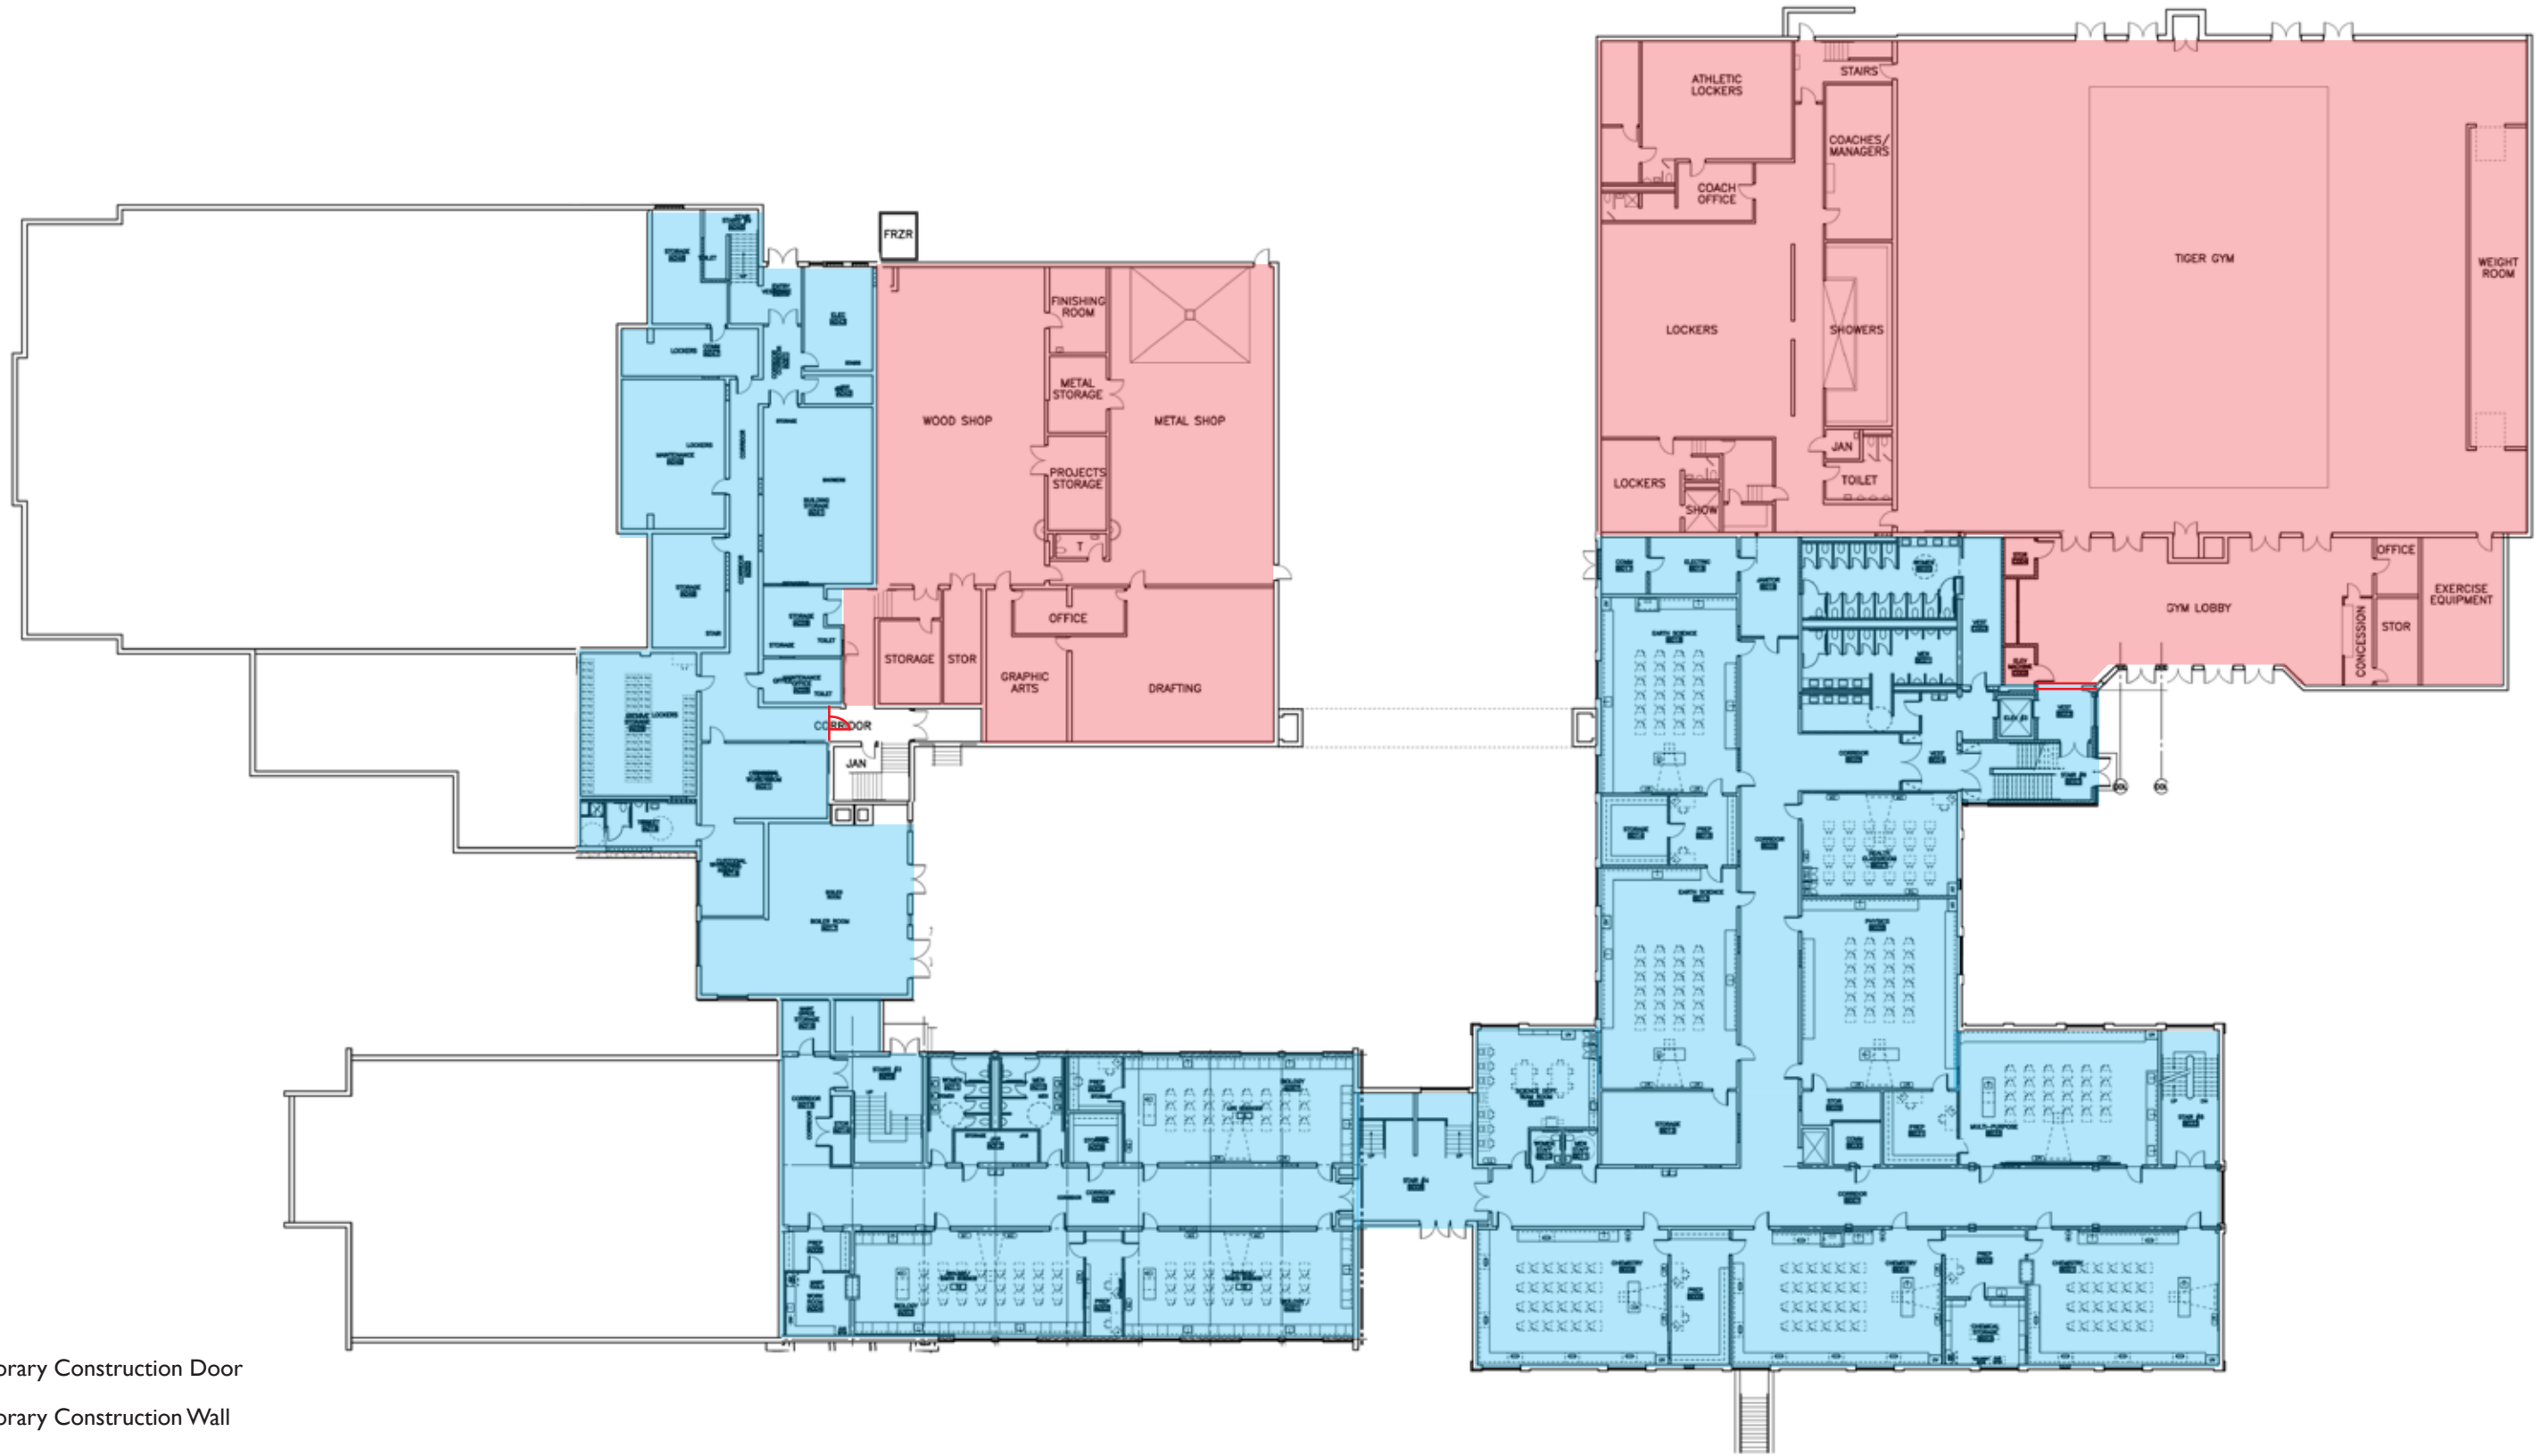

June 9, 2010



**KEY**


-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 8 - Ground Floor April 30, 2012 – June 20, 2012**


- School Re-occupies Fourth Classroom Block at Spring Break
- Start renovations at Shops
- Start renovations at Tiger Gym, Lobby and Lockers



June 9, 2010

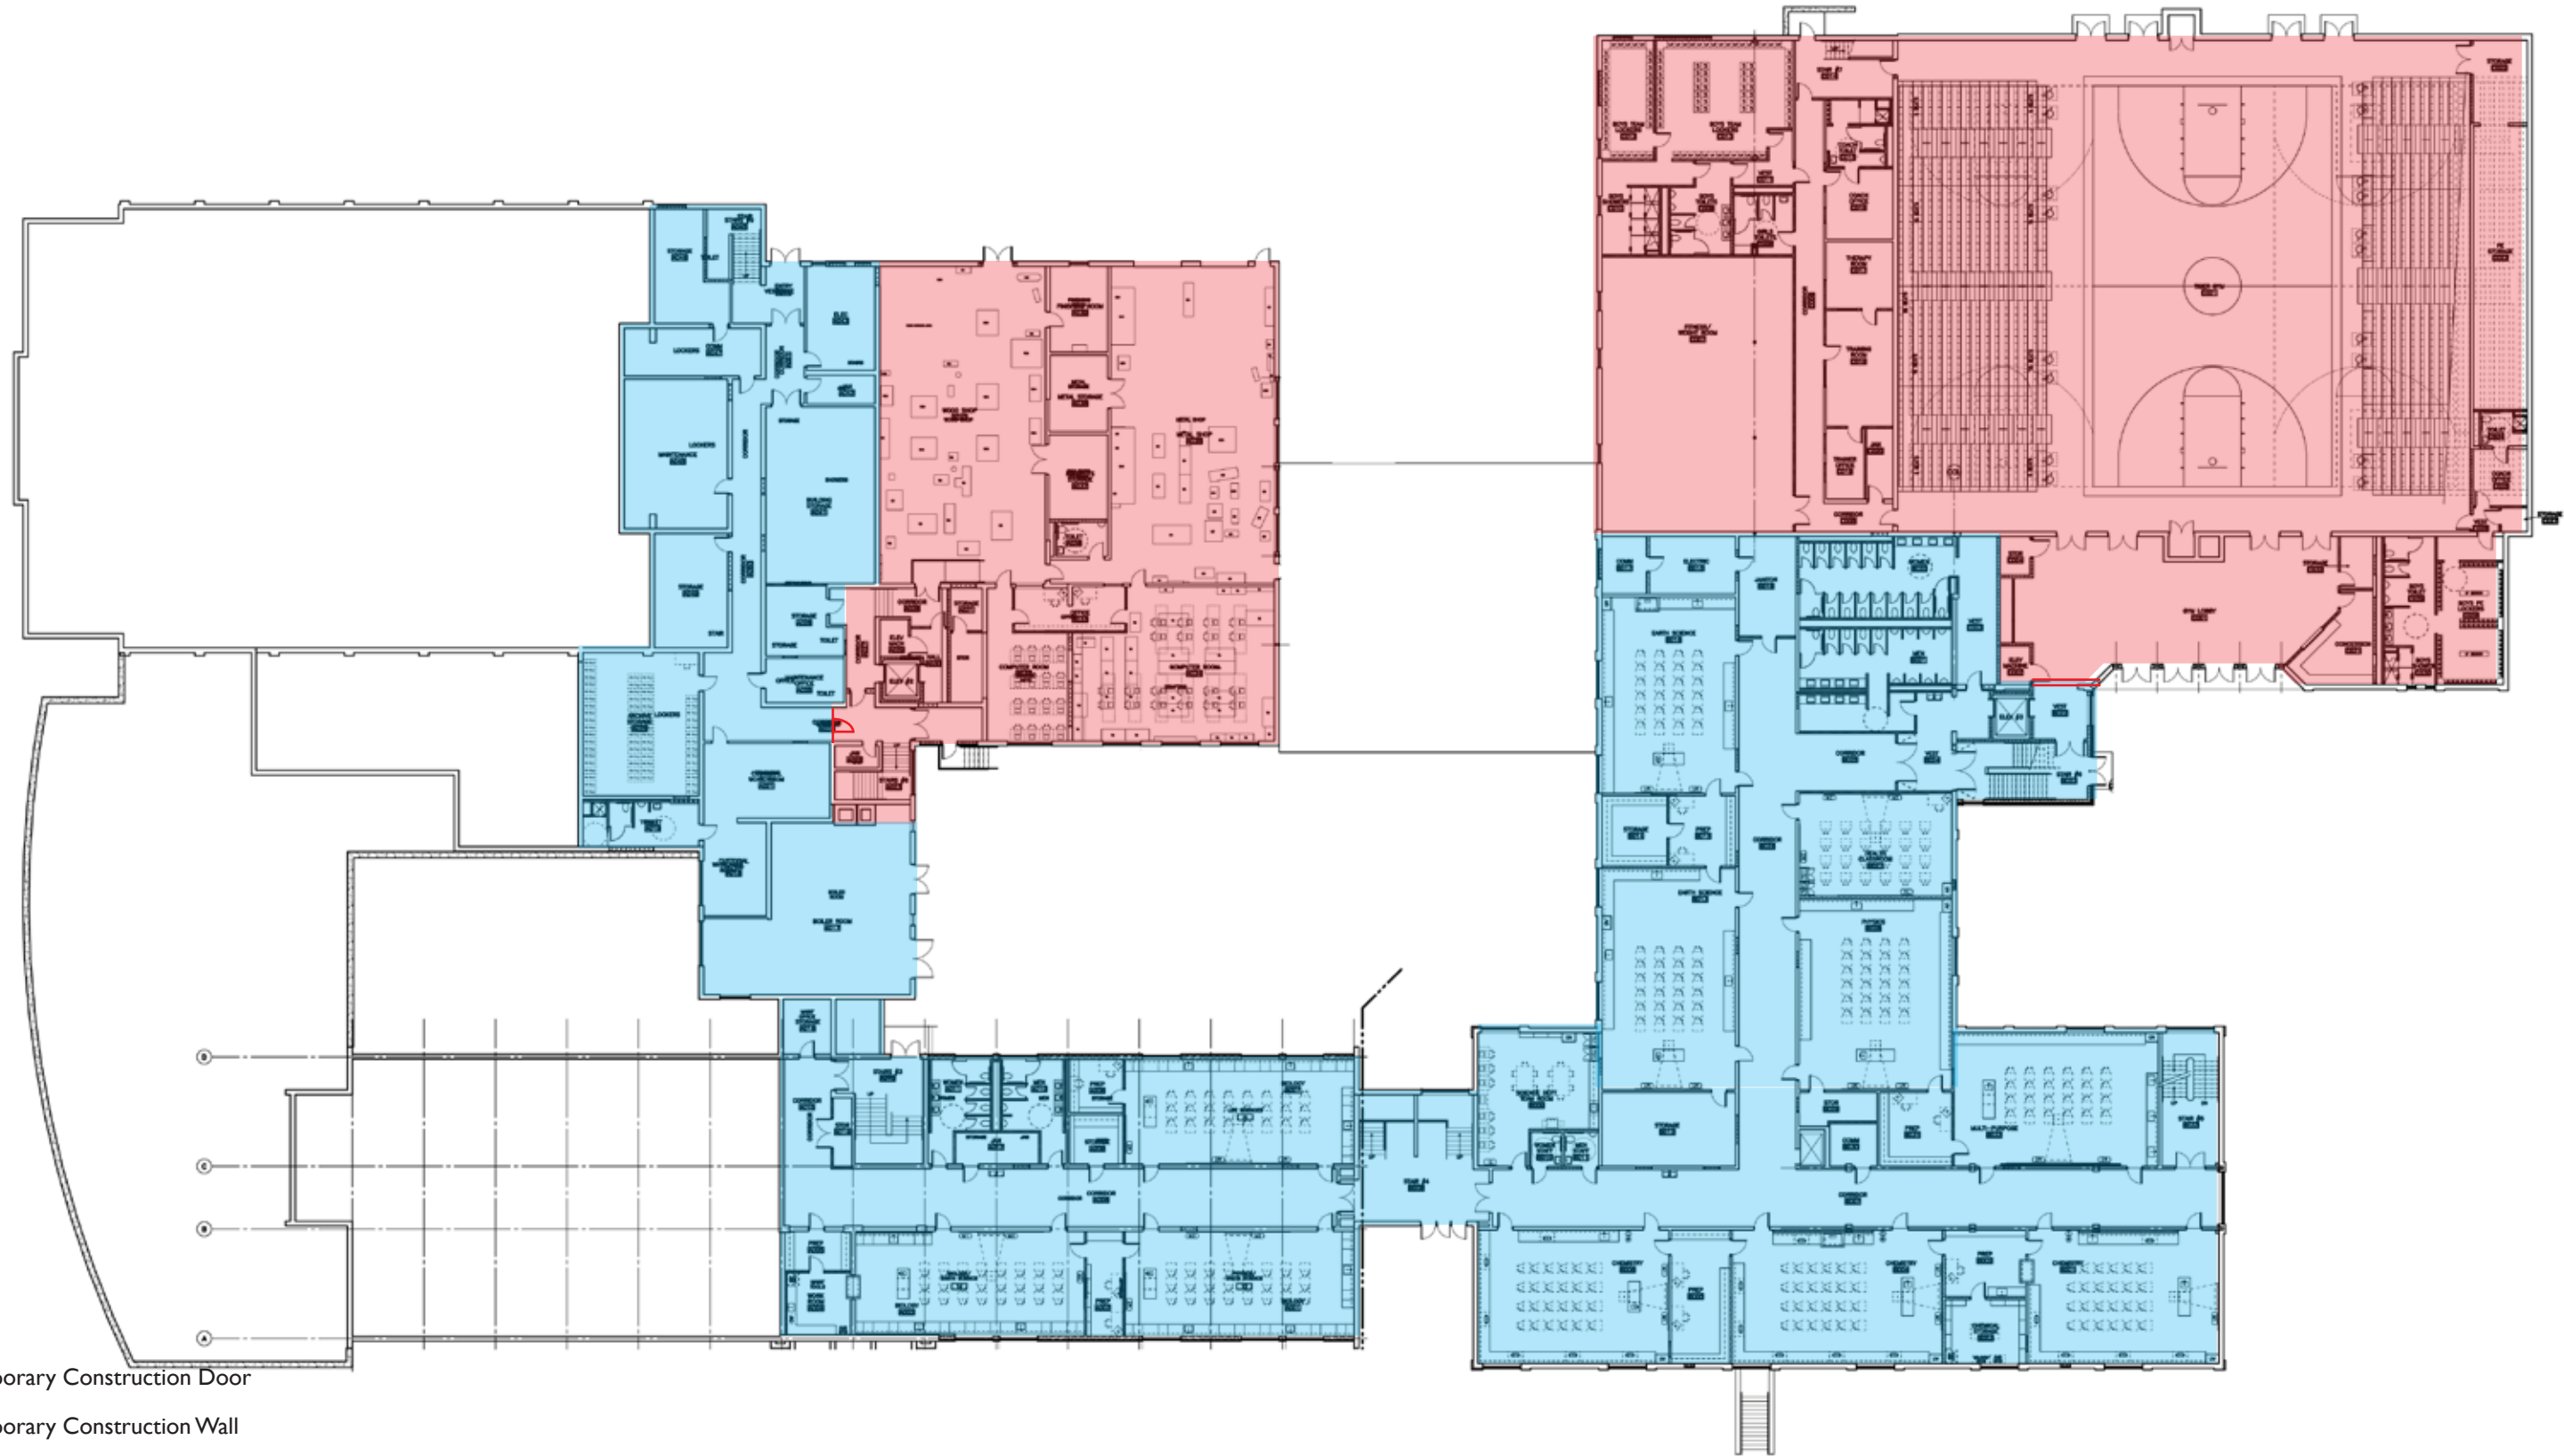

**KEY**

-  Temporary Construction Door
-  Temporary Construction Wall
-  Lock Door & Provide Temporary Signage
-  Construction Area
-  Completed Construction

**Phase 9 - Ground Floor June 21, 2012 – August 24, 2012**

- Renovate Shops
- Renovate Tiger Gym, Lobby and Lockers
